

**NORTH YORK GENERAL HOSPITAL  
SOMATOM DEFINITION FLASH CT**

December 13, 2013

**Previous Week Progress**

- 1 Flooring is complete
- 2 Pot lights are installed
- 3 Equipment delivery was completed and installation has progressed well

**Next Week Progress**

- 1 Closet door installations
- 2 Disconnect finishing
- 3 Roof tip structure installation
- 4 Condenser Installation, connection and commissioning
- 5 X-Ray on lights to be installed
- 6 Final touch up painting
- 7 Installation of patient lift system
- 8 Millwork production continues - Millwork install date for upright storage units will be mid - January

**Jeff Cumming,  
Site Supervisor**

**PROJECT VISUALS**




1



2



3

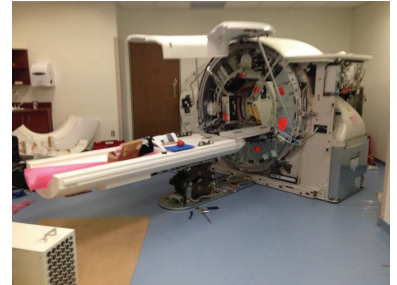

4



5



6
